


Fire Facilities and Emergency Response Levy Schedule Status Thru February 8, 2008

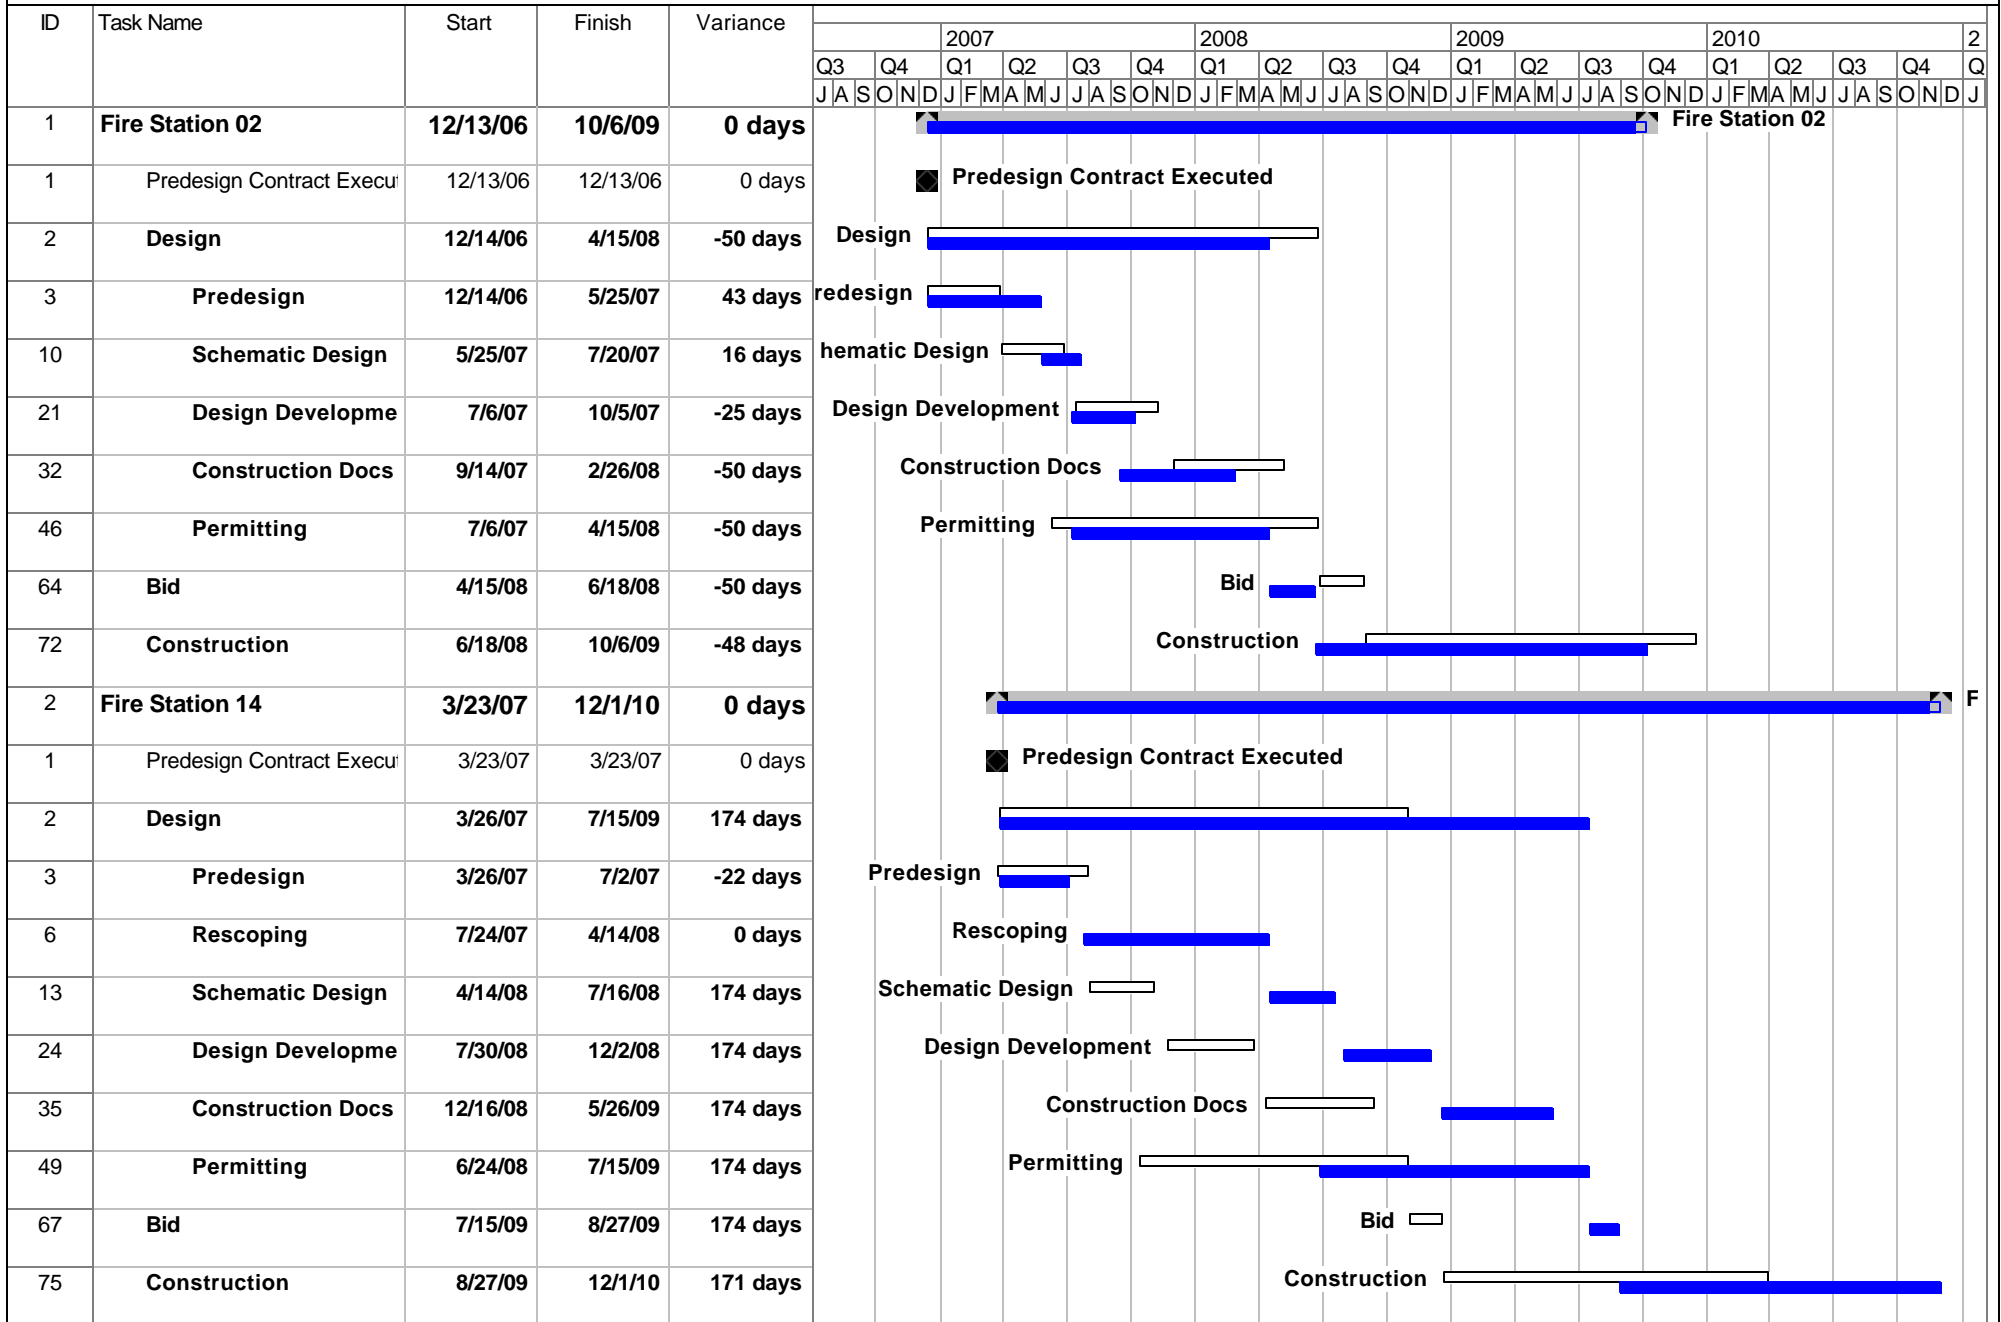

Project: LevyProjectMaster
Date: 2/12/08

Project Summary	Baseline Milestone	Milestone	External Milestone
Critical Summary	Baseline Summary	Summary	External Tasks

Fire Facilities and Emergency Response Levy Schedule Status Thru February 8, 2008

ID	Task Name	Start	Finish	Variance	Schedule																											
					2007							2008							2009							2010						
					Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
3	Fire Station 17	8/23/06	11/30/09	0 days																												
1	Predesign Contract Execut	8/23/06	8/23/06	0 days																												
2	Design	8/23/06	7/14/08	48 days																												
3	Predesign	8/23/06	3/6/07	21 days																												
11	Schematic Design	1/27/07	7/12/07	46 days																												
23	Design Developme	7/12/07	12/21/07	63 days																												
36	Construction Docs	12/21/07	5/27/08	50 days																												
51	Permitting	6/1/07	7/14/08	48 days																												
72	Bid	7/14/08	8/26/08	48 days																												
80	Construction	8/26/08	11/30/09	38 days																												
4	Fire Station 28	8/22/06	12/8/09	0 days																												
1	Predesign Contract Execut	8/22/06	8/22/06	0 days																												
2	Design	8/23/06	3/5/08	-9 days																												
3	Predesign	8/23/06	12/29/06	0 days																												
10	Schematic Design	12/29/06	4/3/07	0 days																												
21	Design Developme	4/17/07	8/31/07	31 days																												
32	Construction Docs	8/31/07	1/14/08	-14 days																												
46	Permitting	2/15/07	3/5/08	-9 days																												
62	Bid	3/5/08	4/17/08	-9 days																												
70	Construction	4/17/08	12/8/09	78 days																												

Project: LevyProjectMaster
Date: 2/12/08

Project Summary	Baseline Milestone	Milestone	External Milestone
Critical Summary	Baseline Summary	Summary	External Tasks

Fire Facilities and Emergency Response Levy Schedule Status Thru February 8, 2008

ID	Task Name	Start	Finish	Variance	Schedule																														
					2007							2008							2009							2010									
					Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4													
					J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J
5	Fire Station 30	3/22/07	5/6/10	0 days																															
1	Predesign Contract Execu	3/22/07	3/22/07	0 days																															
2	Design	4/3/07	12/18/08	26 days																															
3	Predesign	4/3/07	9/14/07	25 days																															
10	Schematic Design	9/14/07	1/22/08	46 days																															
21	Design Developme	1/22/08	5/21/08	36 days																															
32	Construction Docs	5/21/08	10/27/08	26 days																															
46	Permitting	6/21/07	12/18/08	26 days																															
62	Bid	12/18/08	2/4/09	26 days																															
70	Construction	2/4/09	5/6/10	23 days																															
6	Fire Station 31	8/17/06	12/19/08	0 days																															
1	Predesign Contract Execu	8/17/06	8/17/06	0 days																															
2	Design	8/18/06	12/12/07	-30.5 days																															
3	Predesign	8/18/06	3/26/07	18 days																															
10	Schematic Design	4/9/07	5/22/07	15 days																															
21	Design Developme	5/18/07	8/9/07	20 days																															
32	Construction Docs	8/13/07	12/12/07	9.5 days																															
46	Permitting	7/2/07	11/21/07	-43 days																															
53	Bid	12/19/07	2/4/08	-26.5 days																															
61	Construction	2/4/08	12/19/08	-4.5 days																															

Project: LevyProjectMaster
Date: 2/12/08

Project Summary		Baseline Milestone		Milestone		External Milestone	
Critical Summary		Baseline Summary		Summary		External Tasks	

