


# Seattle Streetcar Construction Timeline

*Downtown Retail Core, Westlake Corridor between Olive Way and Virginia Street*

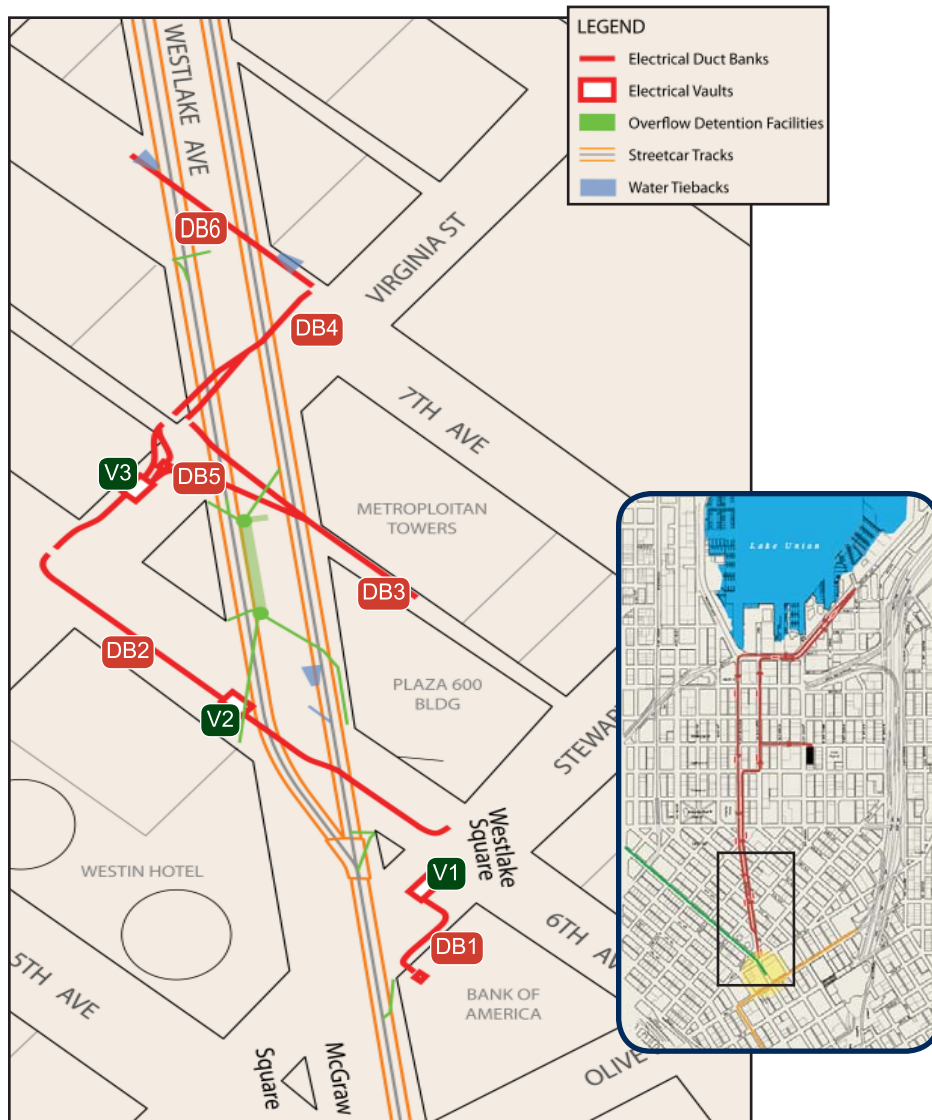

## Electrical Vaults

- V1 ✓ Stewart Street Vault Installation
- V2 ✓ Westlake Avenue & 6th Street Vault Installation
- V3 ✓ Virginia Street Vault Installation

## Electrical Duct Banks

- DB1 ✓ Stewart Street, between Westlake Avenue and 6th Avenue
- DB2 ✓ 6th Avenue, between Stewart Street and Virginia Street
- DB3 ✓ 6th Avenue Alley, between Stewart Street and Westlake Avenue
- DB4 Virginia Street, between 6th Avenue and 7th Avenue  
**Complete by November 22, 2006**  
*\*Note: November 2nd thru November 22nd, Virginia Street, between 4th and Westlake Avenues, will be closed to eastbound traffic.*
- DB5 Westlake and Virginia Intersection  
**Complete by November 22, 2006**
- DB6 7th Avenue, between Virginia Street and Westlake Avenue  
**Complete by January 2007**

## Water Work

- Water Tiebacks ✓ Along Westlake Avenue, between 6th and 9th Avenues
- Detention Facility Westlake Detention Facility Installation  
**Scheduled for 1st quarter 2007**

## Streetcar

- Trackway Installation Westlake Avenue, between Olive Way and Denny Street  
**Scheduled for February 2007 to August 2007**

## Roadway Improvements

- Street Repaving Westlake Avenue, between Olive Way and Denny Street  
**Scheduled to start spring of 2007**

✓ "Substantial Completion" means full and unrestricted use of facility, only minor incidental work remains. Facility accessible to normal vehicular or traffic routes.

[www.seattle.gov/transportation/streetcarnetwork.htm](http://www.seattle.gov/transportation/streetcarnetwork.htm)

Questions: Contact:  
**Josh Stepherson, Community Liaison**  
 Seattle Department of Transportation  
 (206) 684-3136  
[josh.stepherson@seattle.gov](mailto:josh.stepherson@seattle.gov)
