

Mercer Corridor Project: West Phase

Project update



Seattle Freight Advisory Board Briefing

Eric Tweit

April 15, 2014

SDOT's mission & vision

Mission: delivering a first-rate transportation system for Seattle.




Vision: a vibrant Seattle with connected people, places, and products.

SDOT's values




Presentation overview

- Project description
- Schedule
- Construction update
- Existing conditions
- Upcoming changes
- Broad St. closure

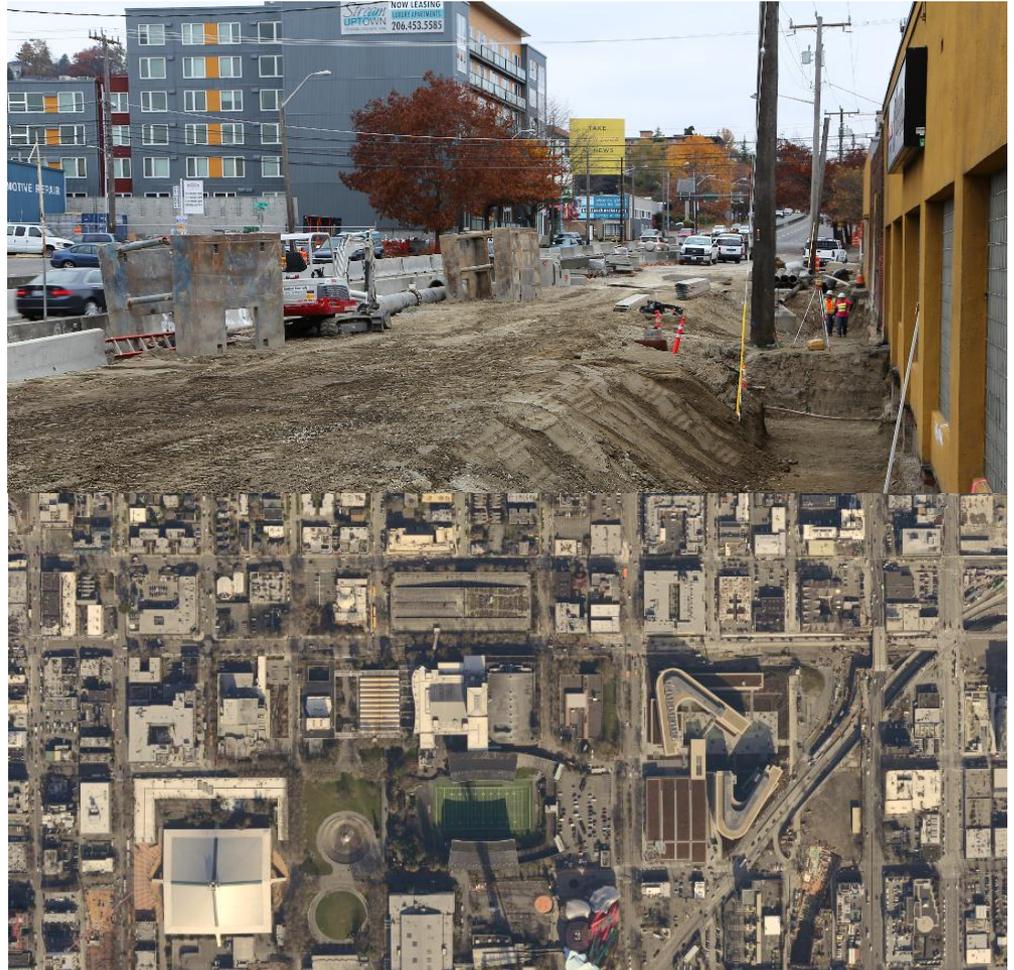

Project description

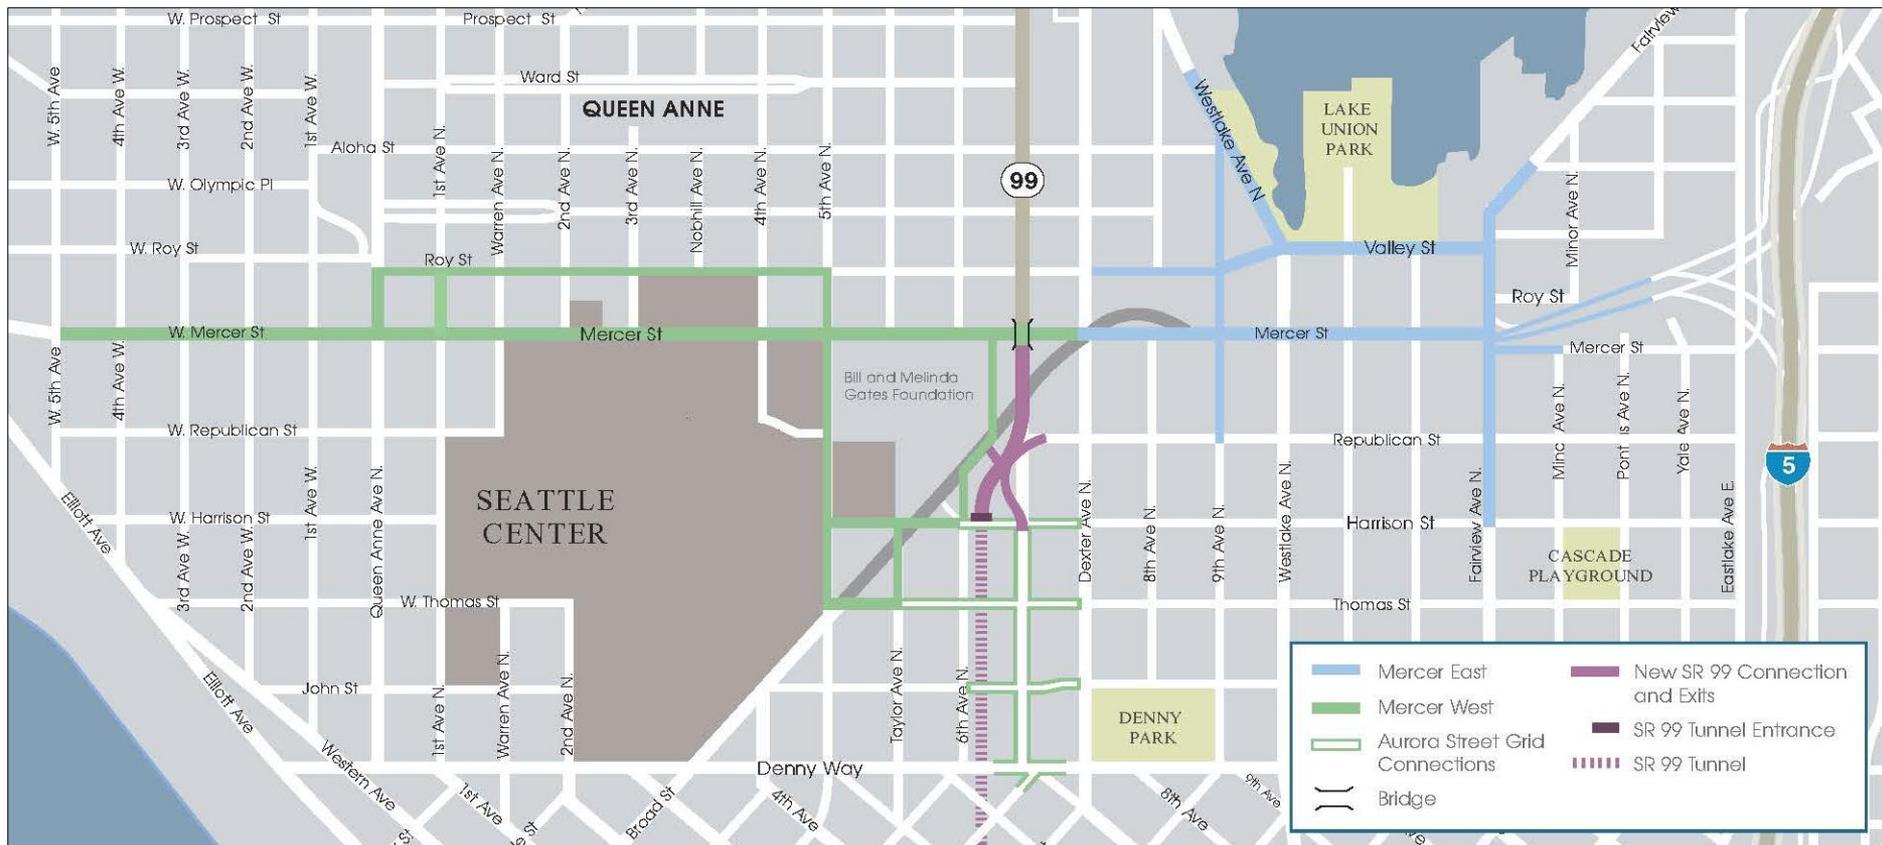


A better roadway for everyone


- Wider sidewalks
- Bicycle path
- Two-way traffic on Mercer and Roy streets
- Replace SR 99 Bridge



Project schedule

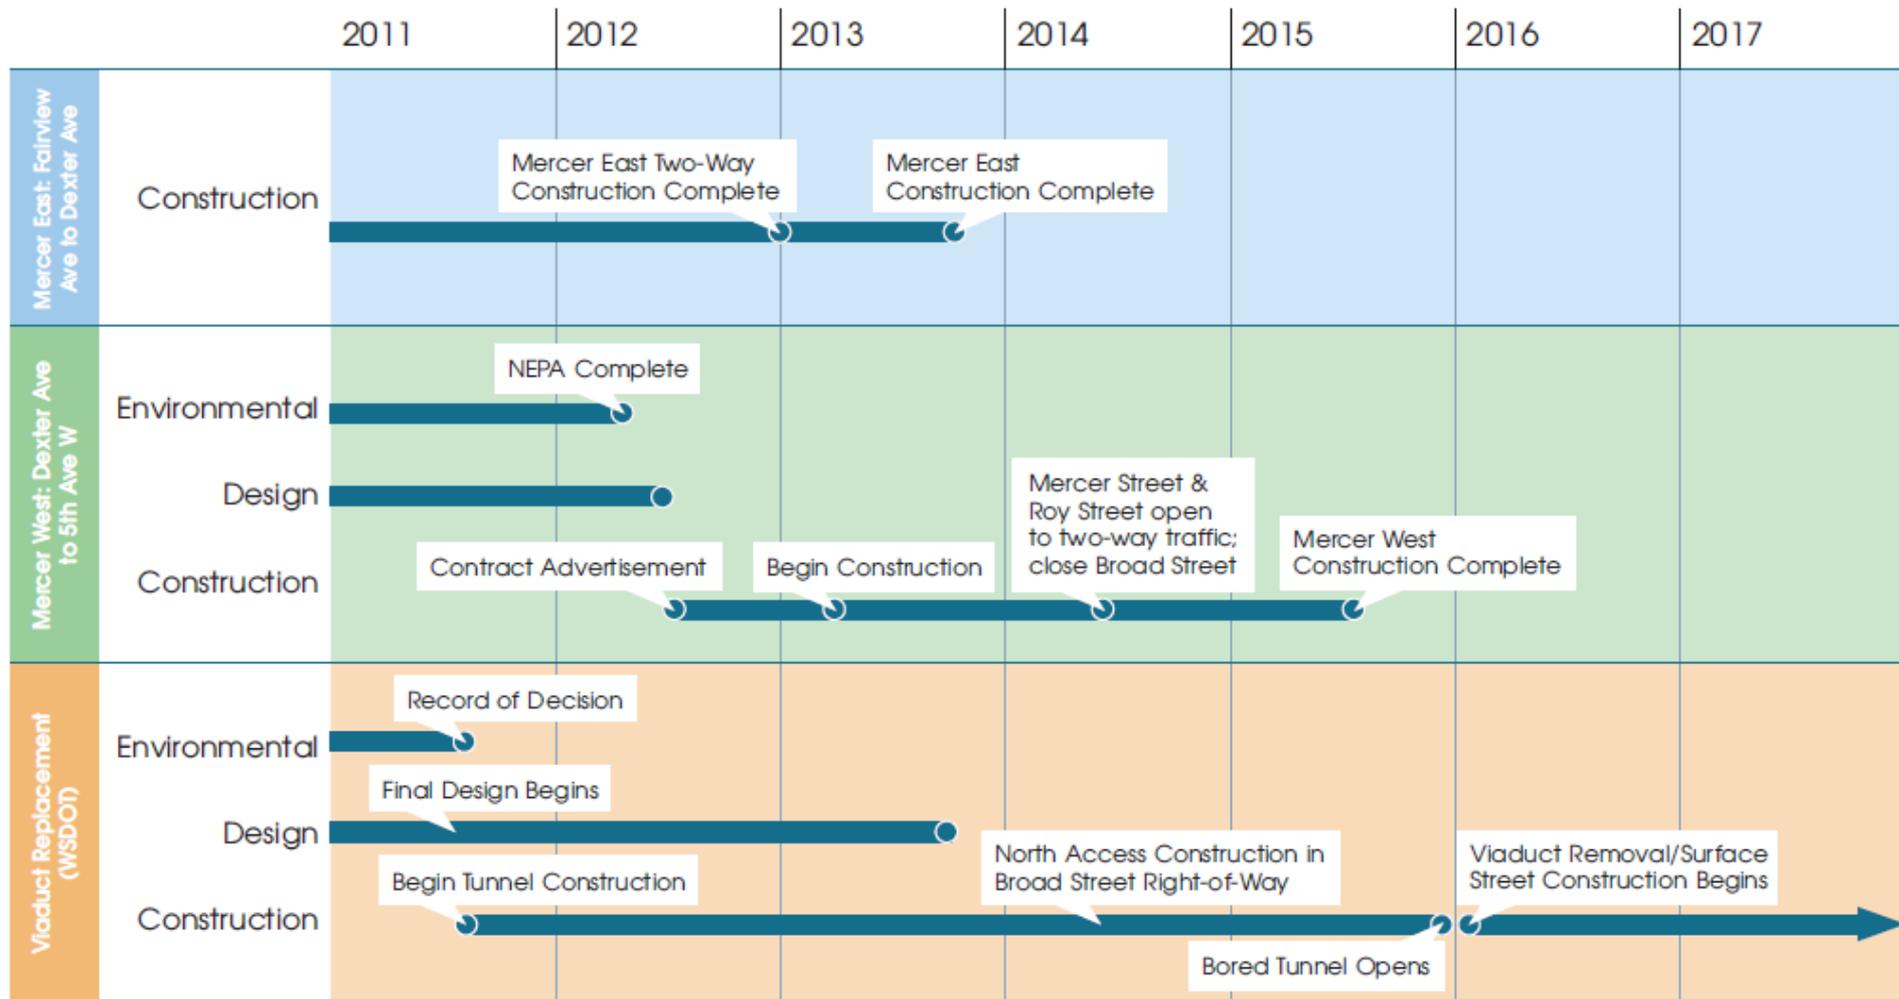


Existing conditions

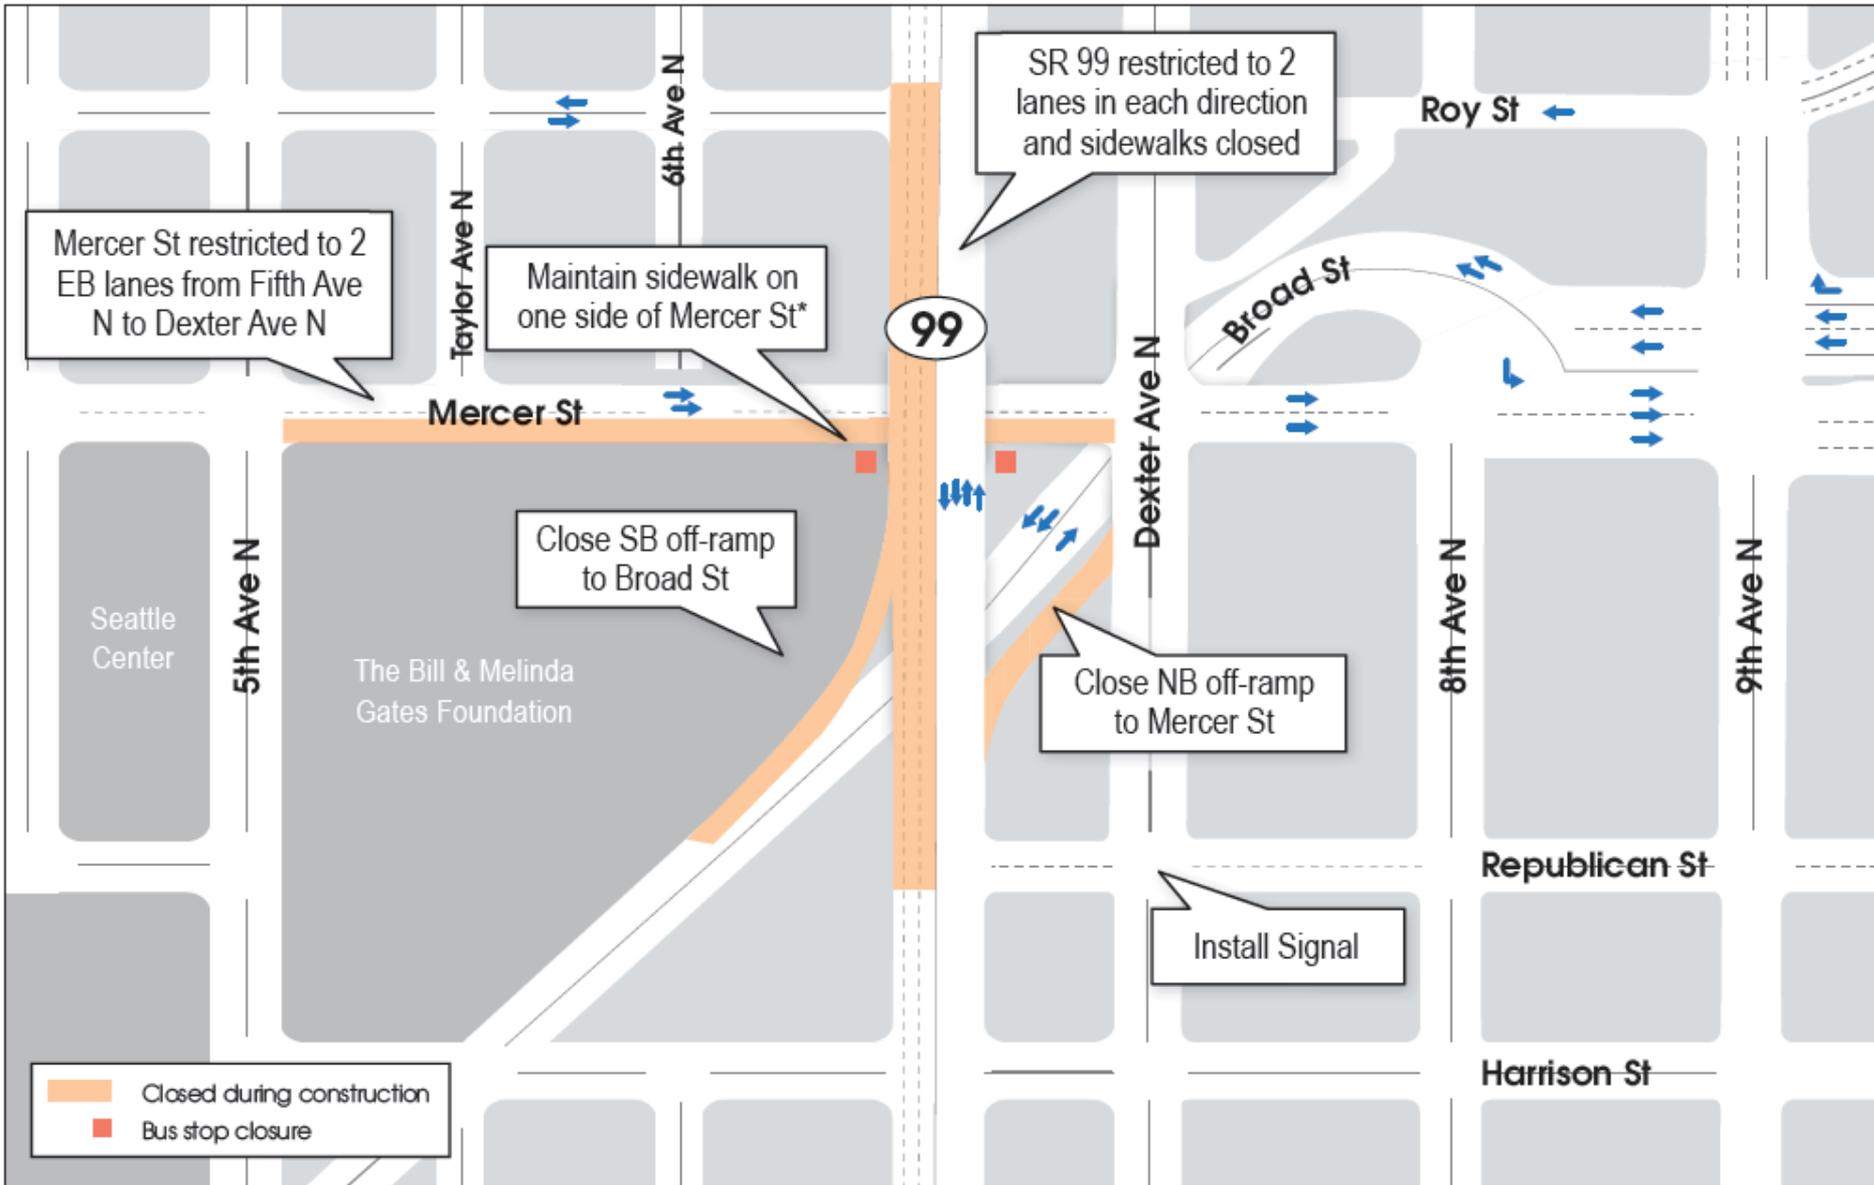

Construction Update

Mercer underpass

- Replaced bridge over SR 99
- Updated utilities
- Widened Mercer St. to the south

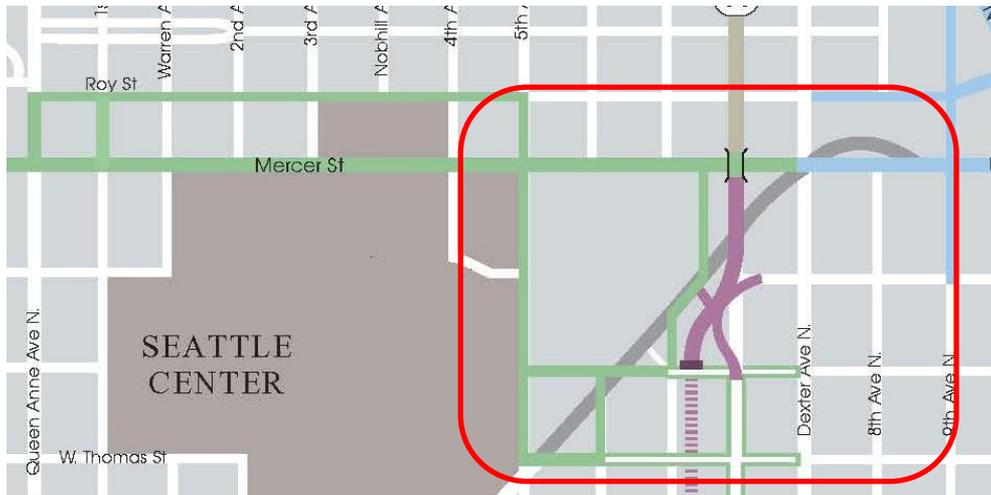

Construction Update

Queen Anne Ave. N to 5th Ave. N

- New signals
- ADA improvements
- Improved sidewalks
- New trolley poles & wires




Coming in May and June

- **Mercer and Roy**
 - Two-way between 5th Ave. N and Queen Anne Ave. N
- **Mercer**
 - Modified two-way (two lanes each direction) between 5th Ave. N and 9th Ave. N
- **Broad St.**
 - CLOSED




Phase I

- Restrictions on Queen Anne Ave. N begin
- Restrictions on Mercer St. continue

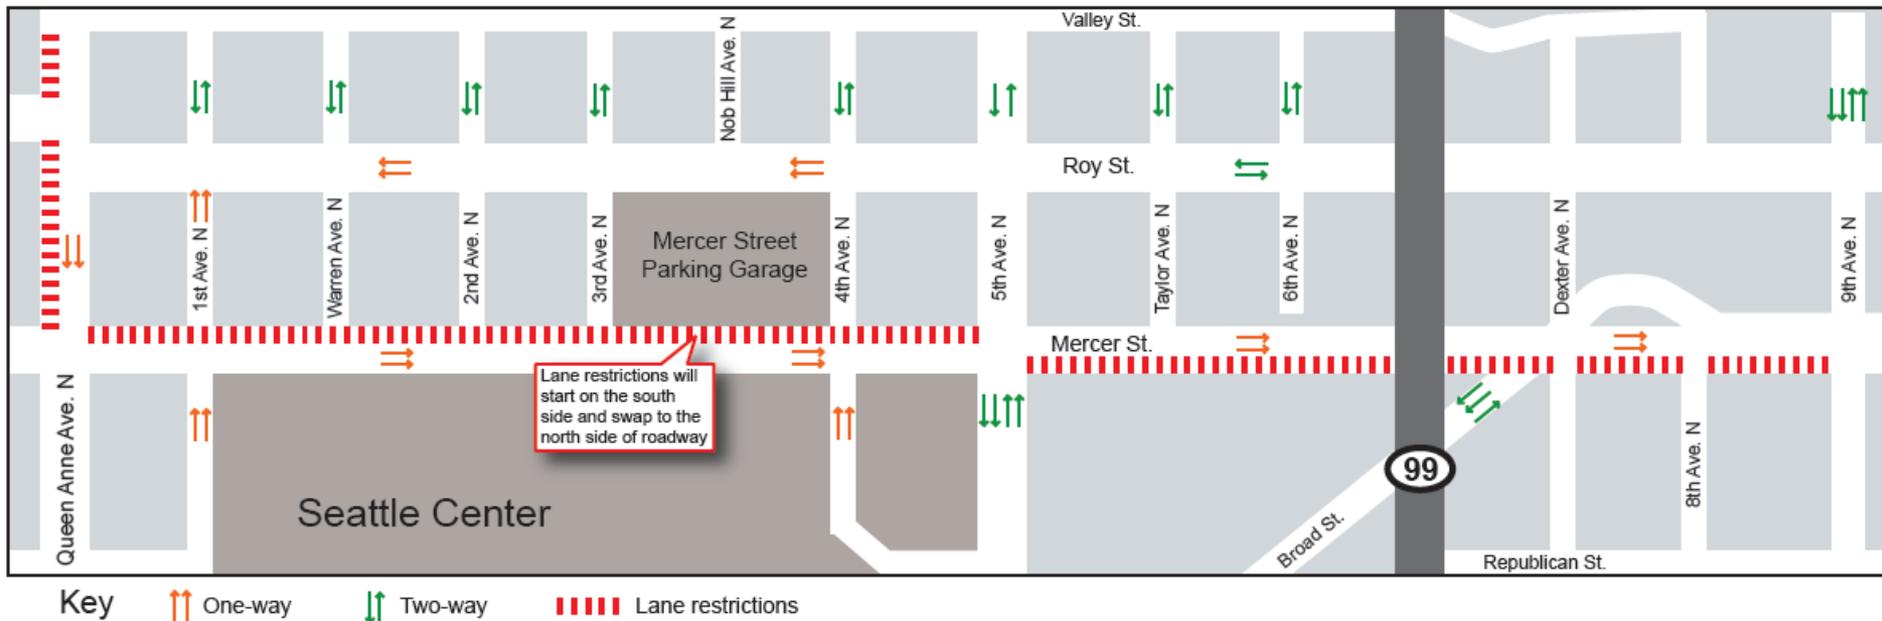


Phase II

- Two-way traffic on Mercer St. west of 5th Ave. N open
- Restrictions on Roy St. begin
- Restrictions on Queen Anne Ave. N continue

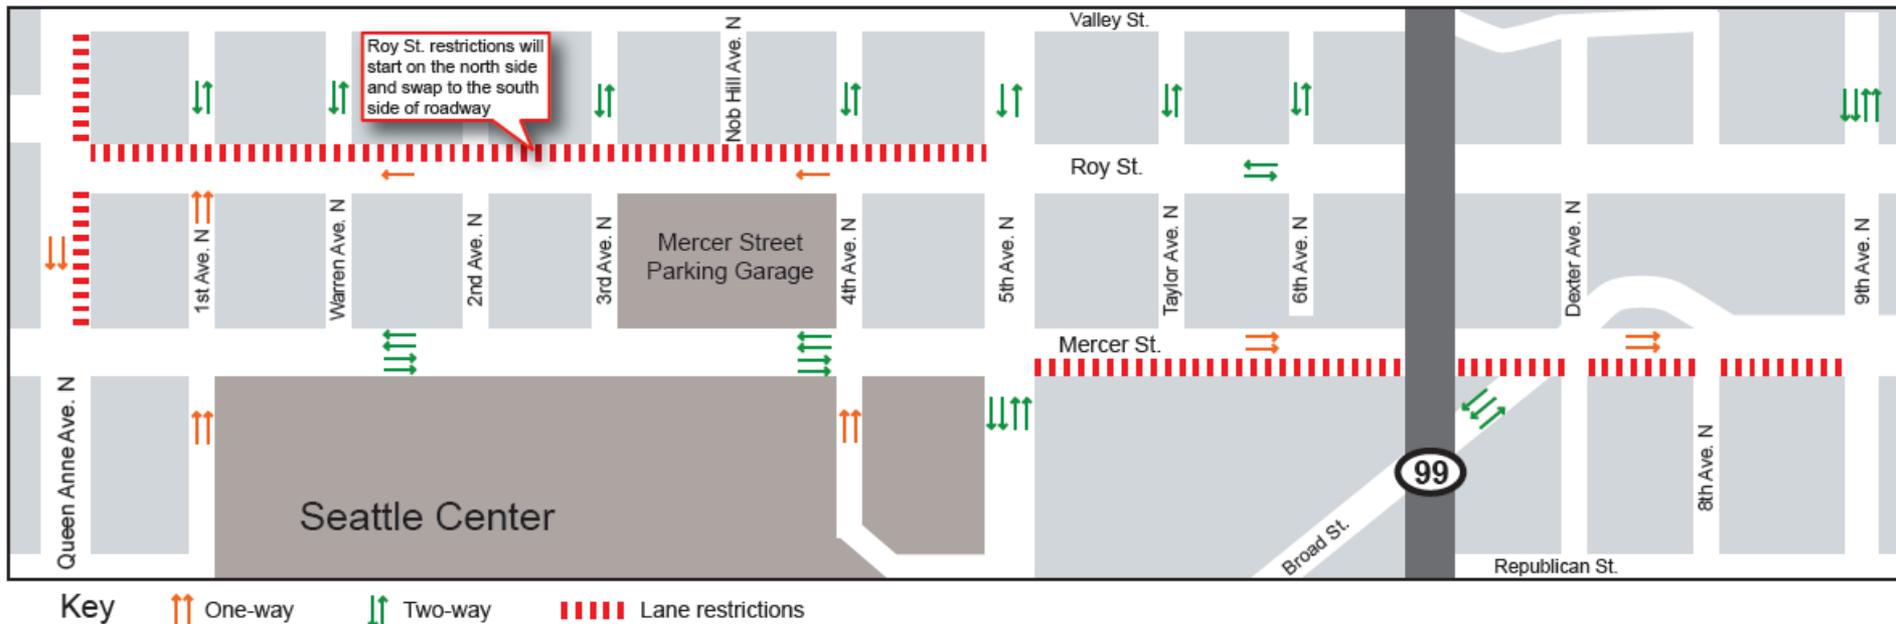

Phase III

- Two-way traffic on Mercer St. east of 5th Ave. N open
- Two-way traffic on Roy St. open
- Two-way traffic on Queen Anne Ave. N open
- Broad St. CLOSED

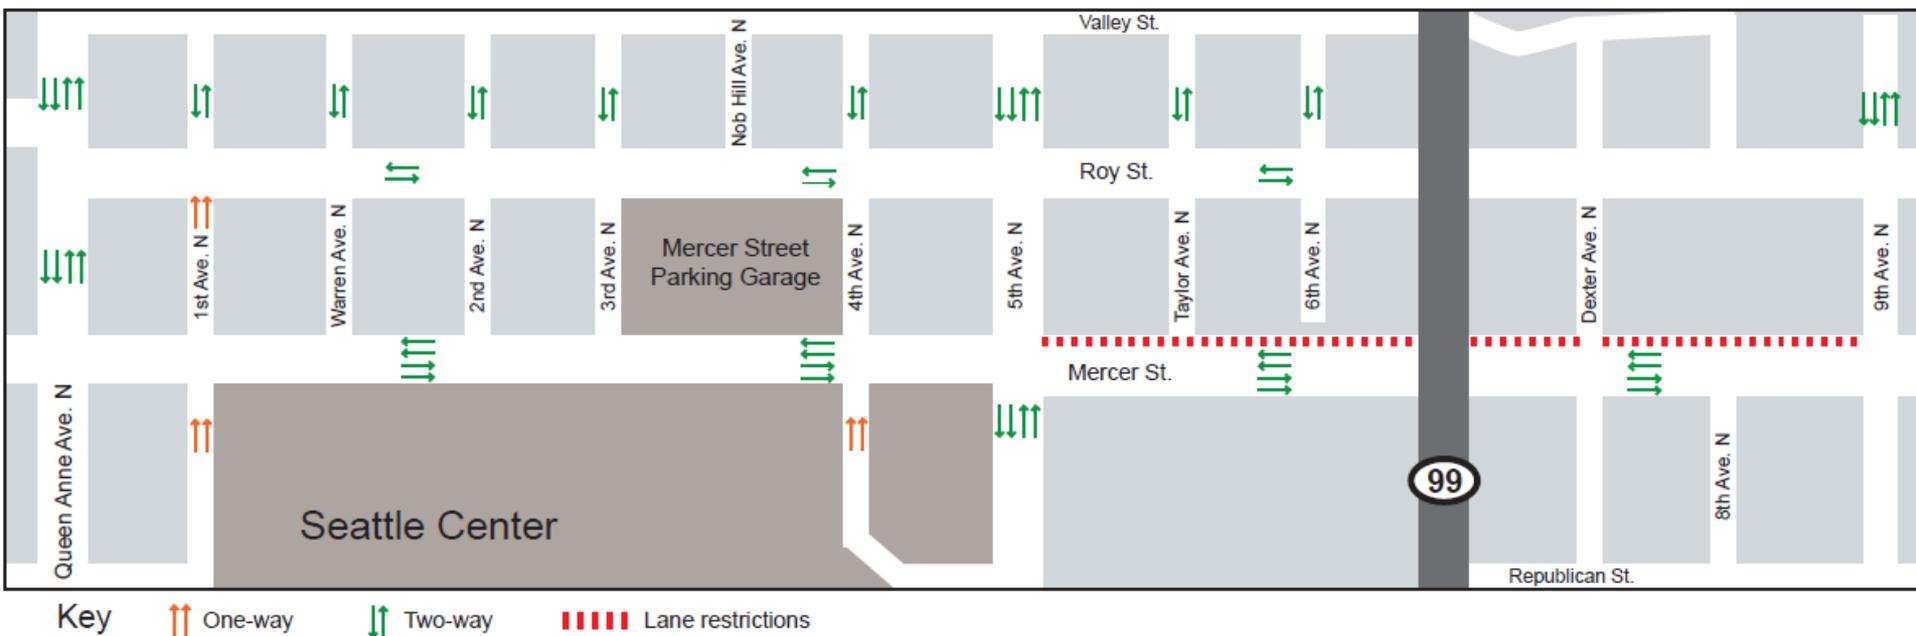


Broad St. closure

Post-closure activities

- Fill Broad St.
- Demo bridge at Mercer St. and Dexter Ave. N
- Install utilities in Mercer St. and Dexter Ave. N
- Capacity restrictions at Mercer St. & Dexter Ave. N
- WSDOT North Access (in Broad St. right-of-way July 1, 2014)



Dexter Ave. N restrictions

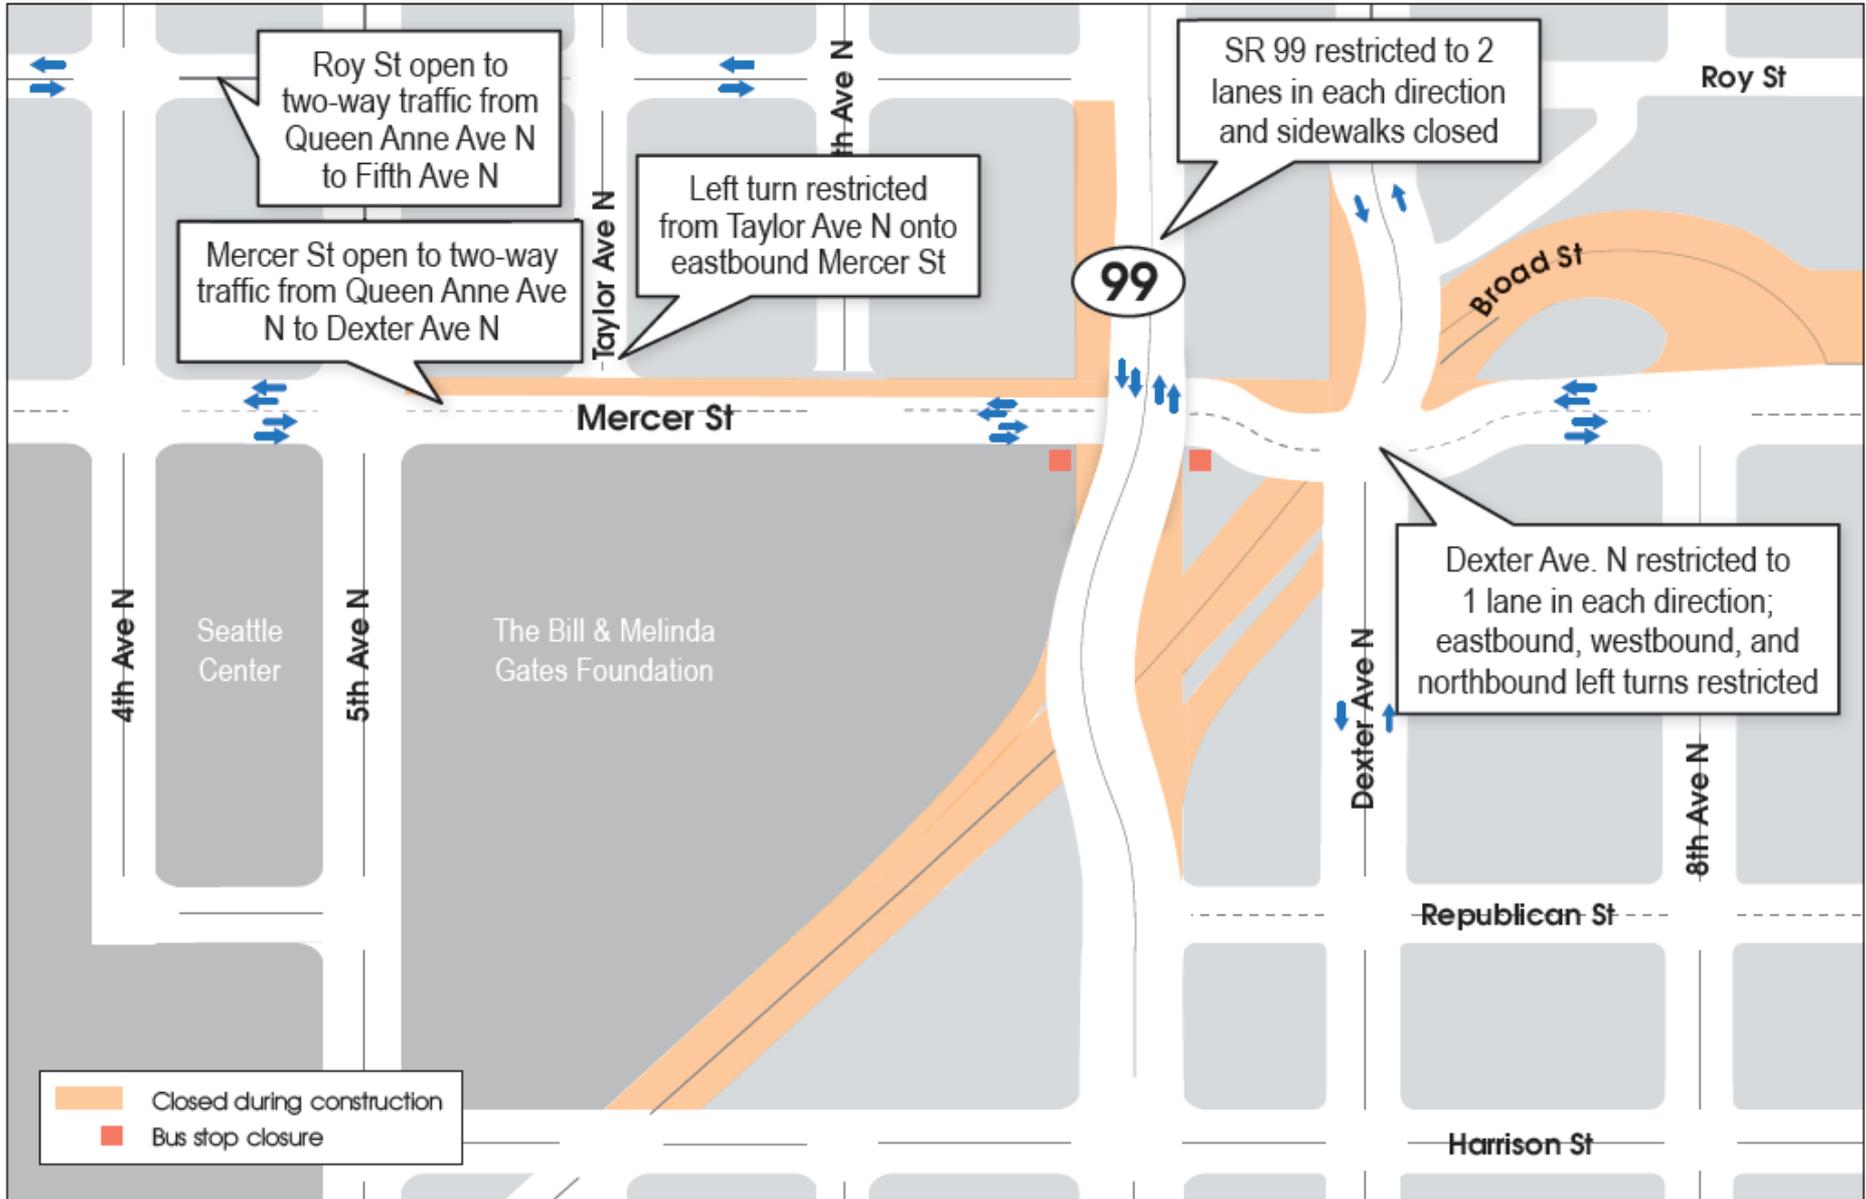

Questions?

mercerinfo@seattle.gov | (206) 419-5818

<http://www.seattle.gov/Transportation/mercercorridor.htm>



Project and Construction Information

Email: mercerinfo@seattle.gov

Phone: (206) 419-5818

Project Office: 701 Dexter Ave. N, Suite 108, Seattle, WA 98109

Website: www.seattle.gov/Transportation/mercercorridor.htm



Thanks for joining us today!

<http://www.seattle.gov/transportation>






Mercer Corridor Project West Phase

The following changes will be implemented at the intersection of Roy Street and Queen Anne Avenue N in Mid-2014:

- Convert Mercer and Roy streets to two-way traffic
- Convert Queen Anne Avenue N to two-way traffic between Roy and Mercer streets
- Install new signal phases and consolidate crosswalks to reduce conflicts between vehicles and pedestrians
- Move the west side curb, including Queen Anne Drive Way, to provide more pedestrian space, increase visibility and reduce crossing distances

LEGEND	
	Traffic Movement
	Traffic Yields (to other traffic and pedestrians)
	Pedestrian Movement
	New Tree
	Existing Tree

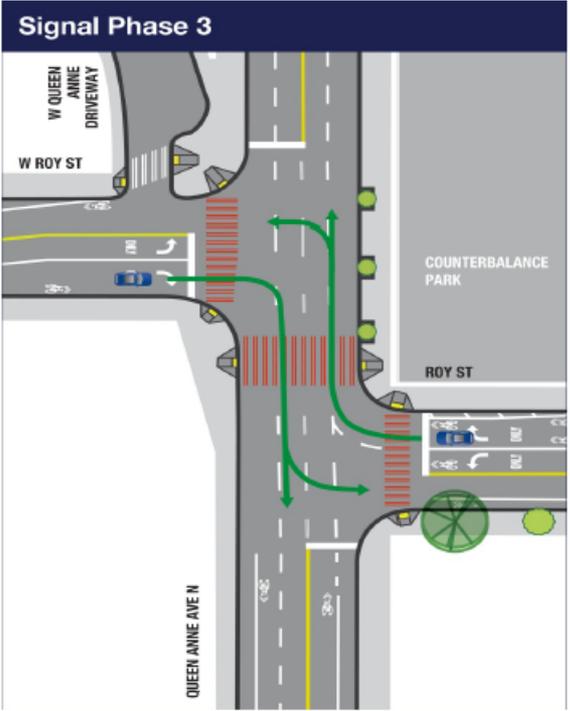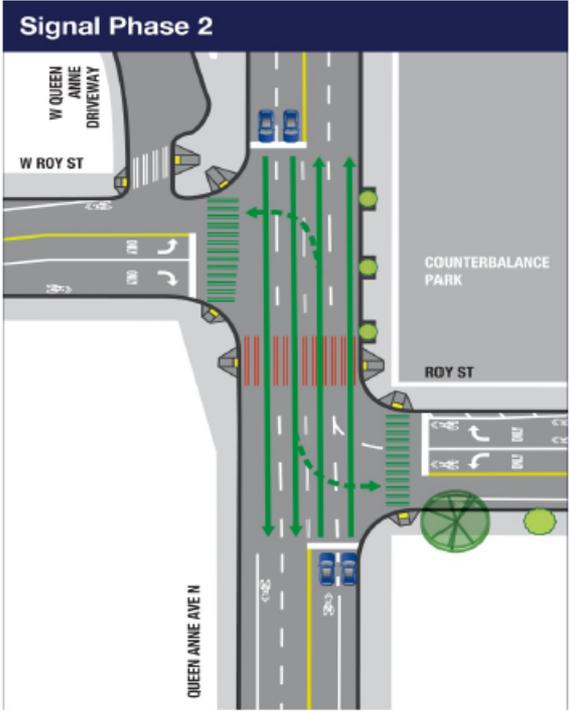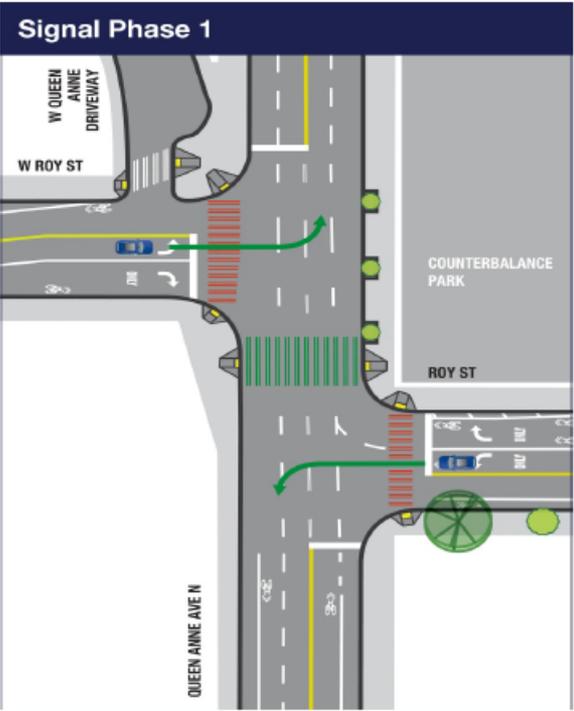

Project & Construction Information: www.seattle.gov/transportation/mercercorridor.htm
 Email: mercercorridor@seattle.gov | Phone: (206) 419-5818



Navigating the Corridor

- Access to I-5 and access to northbound SR 99
- Access to Queen Anne Ave. N from I-5

Mercer West: Fifth Ave N to Dexter Ave N

Access to I-5 and NB SR 99 During Construction



