


APRIL 2012 CONSTRUCTION UPDATE

COMPLETED WORK

- Removed historic windows for restoration off site
- Demolition of Pre-ticketing and old electrical room
- New casting for planters on the west side walkway
- Brick pavers installation for west side walkway
- Historic lamps "Gumbies" installation on Jackson Plaza Balustrade
- New baggage conveyers installed



An electrician installing a lamp post

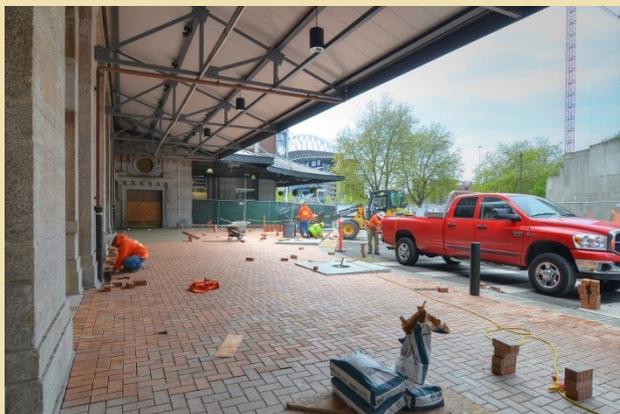

Brick pavers installed. Planters foundation casted.



Baggage conveyer partially installed



LED modules were chosen for longevity and efficiency. Each lamp post stands 6.5' tall and weighs 527 lbs. Each requires over 4 hours to install.



Pre-ticketing and electrical room demolition and exploration. Historic elements saved for restoration.

UPCOMING WORK

- Complete brick pavers installation
- Finish conveyers installation
- Complete walls in temporarily waiting room
- Install 3rd floor access platform
- New structural steel deliveries
- Relocate Amtrak operations



For more details, check out the King Street Station Web site:

<http://www.seattle.gov/transportation/kingstreet.htm>



To remove your name from our mailing list, please [click here](#).

Questions or comments? E-mail us at trevina.wang@seattle.gov or call 206-684-3072

