| ID | Task Name | Duration | Start | Finish | Predecessors | % Complete |
|---|---|---|---|---|---|---|
| 1 | **Fire Station 11** | **1006 days** | **Thu 4/19/12** | **Fri 4/15/16** | | **98%** |
| 2 | PreDesign | 314 days | Thu 4/19/12 | Thu 7/18/13 | | 100% |
| 3 | Scope Alignment | 106 days | Thu 7/19/12 | Wed 12/19/12 | | 100% |
| 4 | Design | 245 days | Wed 12/19/12 | Mon 12/9/13 | 3 | 100% |
| 5 | Bid | 135 days | Tue 12/10/13 | Mon 6/23/14 | 4 | 100% |
| 6 | Construction | 207 days | Mon 6/23/14 | Fri 4/17/15 | 5 | 100% |
| 7 | Closeout | 110 days | Mon 4/20/15 | Tue 9/22/15 | 6 | 100% |
| 8 | Warranty | 252 days | Mon 4/20/15 | Fri 4/15/16 | 6 | 90% |
| 9 | **Fire Station 18** | **1122 days** | **Thu 9/13/12** | **Wed 2/22/17** | | **86%** |
| 10 | Design | 485 days | Thu 9/13/12 | Mon 8/18/14 | | 100% |
| 11 | Permitting | 185 days | Tue 1/21/14 | Fri 10/10/14 | 10FS-147 days | 100% |
| 12 | Bid | 71 days | Tue 8/19/14 | Wed 11/26/14 | 10 | 100% |
| 13 | Construction | 420.38 edays | Mon 12/29/14 | Mon 2/22/16 | 12FS+9 days | 100% |
| 14 | Closeout | 86 days | Tue 2/23/16 | Tue 6/21/16 | 13 | 17% |
| 15 | Warranty | 257 days | Tue 2/23/16 | Wed 2/22/17 | 13 | 0% |
| 16 | **Fire Station 22** | **1131 days** | **Mon 1/13/14** | **Fri 6/29/18** | | **25%** |
| 17 | PreDesign | 165 days | Mon 1/13/14 | Fri 9/5/14 | | 100% |
| 18 | Design | 315 days | Mon 9/8/14 | Fri 12/4/15 | 17 | 100% |
| 19 | Bid | 78 days | Fri 12/4/15 | Tue 3/29/16 | 18 | 86% |
| 20 | Construction | 457 edays | Tue 3/29/16 | Thu 6/29/17 | 19 | 0% |
| 21 | Closeout | 31 days | Fri 6/30/17 | Mon 8/14/17 | 20 | 0% |
| 22 | Warranty | 252 days | Fri 6/30/17 | Fri 6/29/18 | 20 | 0% |
| 23 | **Fire Station 26** | **1105 days** | **Wed 2/15/12** | **Thu 6/30/16** | | **94%** |
| 24 | Design | 445 days | Wed 2/15/12 | Mon 11/18/13 | | 100% |
| 25 | Permitting | 32 days | Tue 11/19/13 | Tue 1/7/14 | 24 | 100% |
| 26 | Bid | 196 days | Tue 11/19/13 | Fri 8/29/14 | 24 | 100% |
| 27 | Construction | 209 days | Tue 9/2/14 | Tue 6/30/15 | 26 | 100% |
| 28 | Closeout | 136 days | Wed 7/1/15 | Wed 1/13/16 | 27 | 100% |

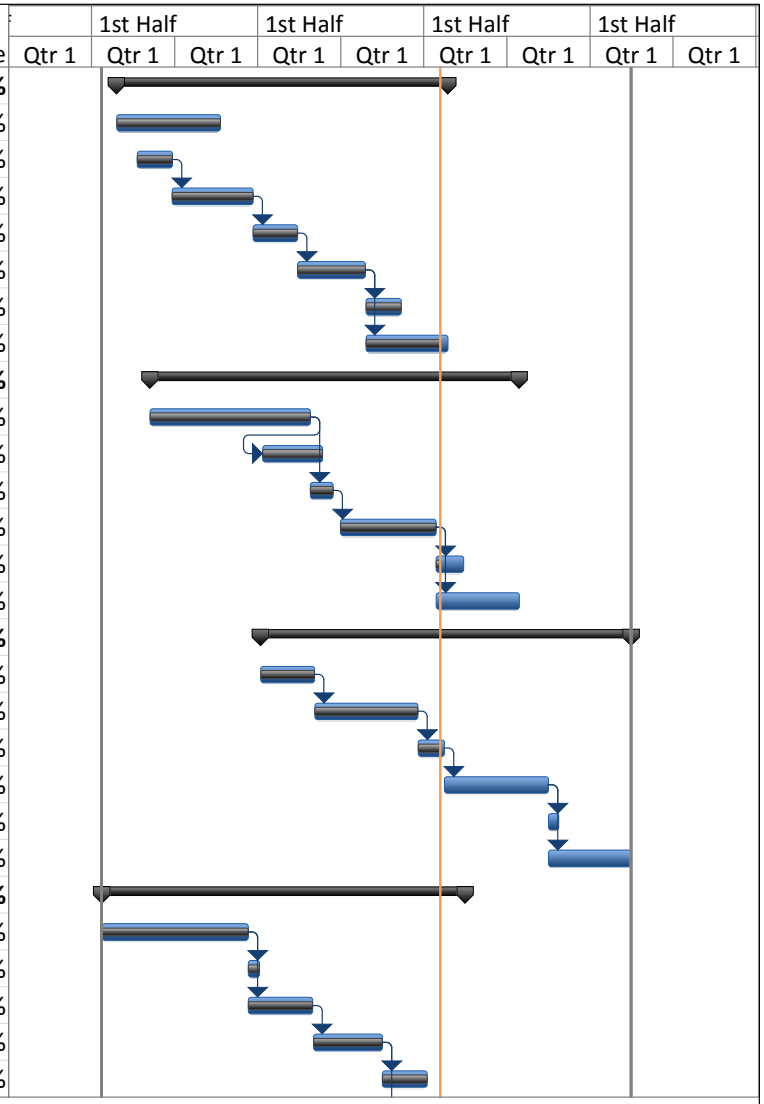


Project: Fire Facilities & Emergenc
Response Program Sched
Date: Mon 3/14/16

| | | |
|---|---|---|
| Task | External Milestone | Manual Summary Rollup |
| Split | Inactive Task | Manual Summary |
| Milestone | Inactive Milestone | Start-only |
| Summary | Inactive Summary | Finish-only |
| Project Summary | Manual Task | Deadline |
| External Tasks | Duration-only | Progress |

| ID | Task Name | Duration | Start | Finish | Predecessors | % Complete |
|---|---|---|---|---|---|---|
| 29 | Warranty | 256 days | Tue 6/30/15 | Thu 6/30/16 | 27FS-1 day | 70% |
| 30 | **Fire Station 28 USAR** | **675 days** | **Tue 4/22/14** | **Mon 12/19/16** | | **82%** |
| 31 | Design | 223 days | Tue 4/22/14 | Wed 3/11/15 | | 100% |
| 32 | Permitting | 110 days | Wed 8/13/14 | Wed 4/22/15 | 31FS-93 days | 100% |
| 33 | Bid | 65 days | Thu 3/12/15 | Thu 6/11/15 | 31 | 100% |
| 34 | Construction | 189 edays | Thu 6/11/15 | Thu 12/17/15 | 33 | 100% |
| 35 | Closeout | 98 days | Fri 12/18/15 | Mon 5/9/16 | 34 | 59% |
| 36 | Warranty | 255 days | Fri 12/18/15 | Mon 12/19/16 | 34 | 23% |
| 37 | **Fire Station 29** | **964 days** | **Wed 2/13/13** | **Mon 12/5/16** | | **81%** |
| 38 | PreDesign | 79 days | Wed 2/13/13 | Wed 6/5/13 | | 100% |
| 39 | Design | 340 days | Thu 6/6/13 | Thu 10/9/14 | 38 | 100% |
| 40 | Bid | 101 days | Fri 10/10/14 | Mon 3/9/15 | 39 | 100% |
| 41 | Construction | 189 days | Tue 3/10/15 | Thu 12/3/15 | 40 | 100% |
| 42 | Closeout | 81 days | Fri 12/4/15 | Thu 3/31/16 | 41 | 84% |
| 43 | Warranty | 255 days | Fri 12/4/15 | Mon 12/5/16 | 41 | 27% |
| 44 | **Fire Station 32** | **1378 days** | **Tue 11/6/12** | **Mon 4/23/18** | | **34%** |
| 45 | Design | 723 days | Tue 11/6/12 | Mon 9/21/15 | | 100% |
| 46 | Bid | 108 days | Tue 9/22/15 | Fri 2/26/16 | 45 | 100% |
| 47 | Construction | 420 edays | Mon 2/29/16 | Mon 4/24/17 | 46 | 0% |
| 48 | Closeout | 90 days | Mon 4/24/17 | Tue 8/29/17 | 47 | 0% |
| 49 | Warranty | 252 days | Mon 4/24/17 | Mon 4/23/18 | 47 | 0% |

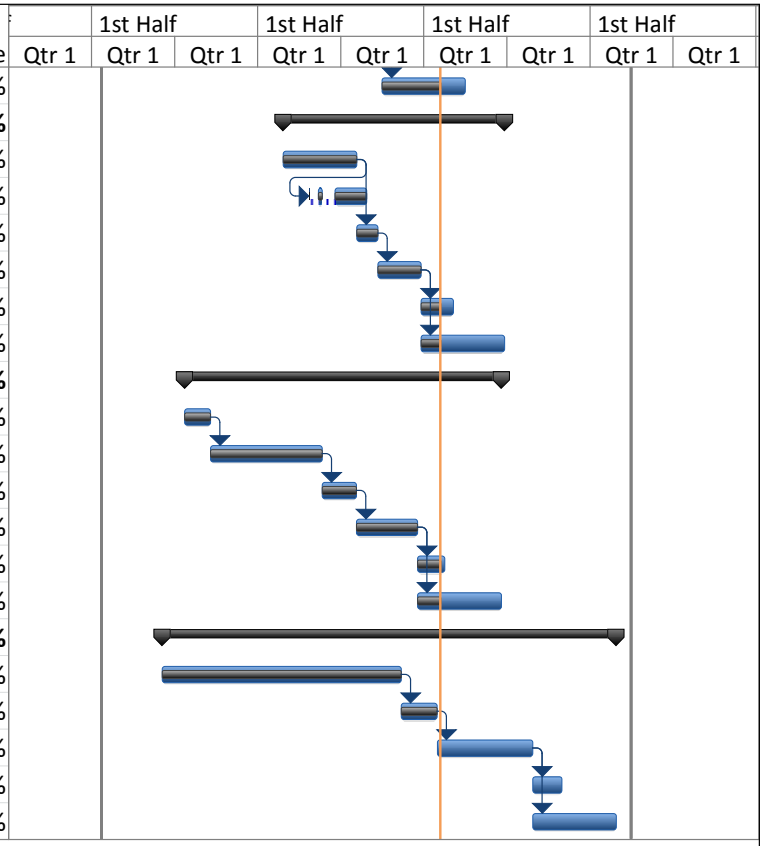


Project: Fire Facilities & Emergenc Response Program Sched
Date: Mon 3/14/16

| | | | | | |
|---|---|---|---|---|---|
| Task | | External Milestone | | Manual Summary Rollup | |
| Split | | Inactive Task | | Manual Summary | |
| Milestone | | Inactive Milestone | | Start-only | |
| Summary | | Inactive Summary | | Finish-only | |
| Project Summary | | Manual Task | | Deadline | |
| External Tasks | | Duration-only | | Progress | |
